Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story points)

Date	04 October 2026
Team ID	SWTID-2026-6870
Project Name	Streamlining IT Procurement: Automating Standard Laptop Orders with Flow Designer
Maximum Marks	5 Marks

Product Backlog, Sprint Schedule, and Estimation

Story points follow the Fibonacci-style scale used in the planning guide: **1** = very easy, **2** = normal, **3** = moderate, **5** = difficult. The project was split into **2 sprints**.

Sprint	Functional Requirement (Epic)	User Story No.	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Flow creation	USN-1	As a flow developer, I can create the flow "Standard laptop task" (Global, Run As System User).	2	High	[Add name]
Sprint-1		USN-2	As a flow developer, I can add the Service Catalog trigger.	1	High	[Add name]
Sprint-1		USN-3	As a flow developer, I can add the Create Catalog Task action with short description, description, Assignment group Hardware and Approval Approved.	3	High	[Add name]
Sprint-1		USN-4	As a flow developer, I can save and activate the flow.	1	High	[Add name]
Sprint-1	Flow assignment	USN-5	As a catalog administrator, I can attach the flow to the Standard Laptop item under Process Engine.	2	High	[Add name]
Sprint-2	Ordering & approval	USN-6	As an employee, I can order a Standard Laptop from Service Catalog > Hardware.	2	High	[Add name]
Sprint-2		USN-7	As an approver, I can approve the request from the Approvers related list.	2	High	[Add name]
Sprint-2	Task verification	USN-8	As a Hardware team member, I can see the catalog task assigned to my group under the Requested Item.	3	High	[Add name]
Sprint-2	Testing & documentation	USN-9	As the project team, we can run functional tests and UAT.	3	Medium	[Add name]
Sprint-2		USN-10	As the project team, we can document the project and results.	2	Medium	[Add name]

Sprint-1 total = 2+1+3+1+2 = **9** story points. Sprint-2 total = 2+2+3+3+2 = **12** story points. Total = **21** story points.

Project Tracker, Velocity & Burndown Chart

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (as on Planned End Date)	Sprint Release Date (Actual)	Velocity (points/day)
Sprint-1	9	7 Days	21 Sep 2026	27 Sep 2026	9	27 Sep 2026	1.29
Sprint-2	12	7 Days	28 Sep 2026	04 Oct 2026	12	04 Oct 2026	1.71

Velocity

Average velocity = Total story points completed ÷ number of sprints = (9 + 12) ÷ 2 = **10.5 story points per sprint**.
Per day, velocity = 21 ÷ 14 days = **1.5 story points per day**.

Burndown Chart

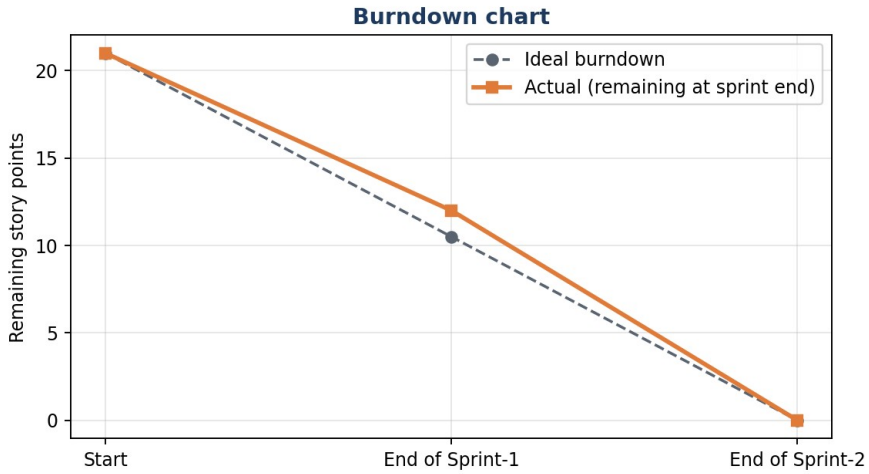


Figure 1: Burndown chart (remaining story points at sprint end)

Sprint dates in this document are planning dates and can be changed to match your actual schedule.
